

Our challenge

Overall goal	Support charities to prioritise their user needs, and prototype and test solutions using, where possible, existing technologies and platforms.
Problem to be solved	Some organisations need to learn more about their users' needs and behaviours to make progress. They need support to identify who they should talk to next and how to validate their riskiest assumptions and questions. Beneficiaries of some of these charities are digitally excluded. Clarity of content, ease-of-use and accessibility are fundamental to addressing the challenges faced by these communities. Some of these charities also have safeguarding considerations due to their audience types.

Context

Who's involved?	We have two cohorts of charities who have been through a discovery phase and would benefit from initial coaching or guidance to help them consolidate what they've learnt so far and further refine their challenge and audience. They'll need some support to work out what their next steps should be - for some this will be more user research, while others will already be well-placed to prototype.
What have they already done?	The charities have already done some prototyping and testing with users, but need additional time and support to further develop and test. This could be technical support to identify and tie various off-the-shelf tools together, iterating on what they've already done, or helping them to create a testing plan.

Expected outcomes for this work

Expected outputs	• Prototypes that have been tested with service users and/or the organisations supporting them. A prototype here might be a product, service, experience or configuration of existing tools. • Insights from research and testing • Documentation of the process and learnings to be openly published and shared with the sector as 'service blueprints'. By service blueprints we mean a map or outline of the different components or steps which make up a service or product. This is so that other charities can reuse them in their own processes, enabling them to use digital at a lower cost/higher pace.
Expected outcomes	• Learned skills and techniques to continue with this work beyond the funding period • Increased teams' digital confidence and capabilities

Progress indicator

Progress updates due monthly

Charities have shared their outputs and learnings openly

Progress updates due monthly

Charities understand how potential solutions will be delivered and sustained

Progress updates due monthly


Charities have tested and validated how potential solutions meet the needs of users

Progress updates due monthly

Charities have identified their riskiest assumptions to test

Progress updates due monthly

Charities have tested prototypes with service users and/or the organisations supporting them

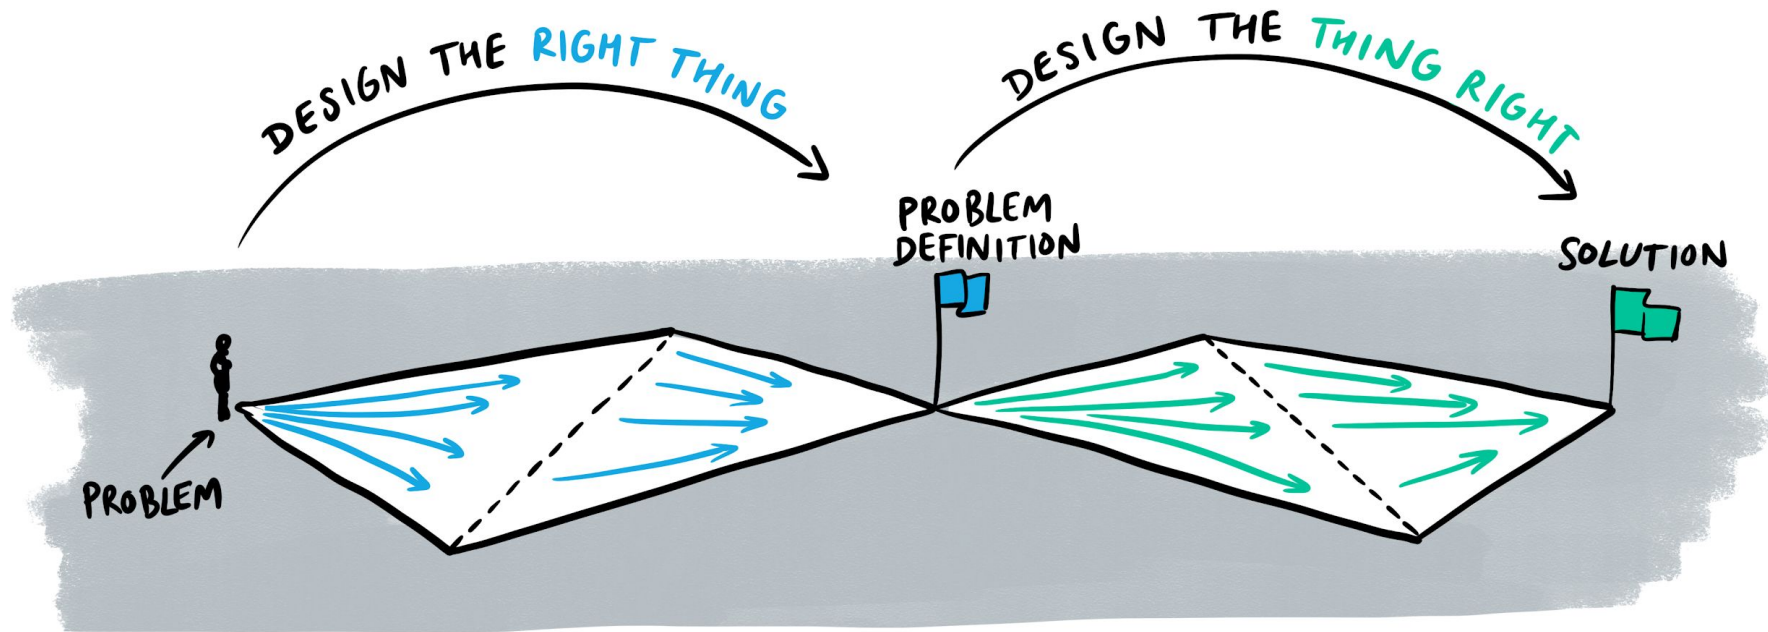

DISCOVER DEFINE DEVELOP DELIVER

DOUBLE DIAMOND

Weekly overview

PREPARE	RESEARCH				DESIGN					WRAP-UP	
	DISCOVER		DEFINE		DEVELOP				DELIVER		
Week Z 01 - 05 Feb	Week 0 08-12 Feb	Week 1 15-19 Feb	Week 2 22-26 Feb	Week 3 01-05 Mar	Week 4 08-12 Mar	Week 5 15-19 Mar	Week 6 22-26 Mar	Week 7 29-02 Apr	Week 8 06 - 09 Apr	Week 9 12-16 Apr	Week 10 19-23 Apr
Catalyst welcome event Team meeting Admin	1:1 meetings Project initiation	Kick-off workshop Audience analysis	Architecture Of Participation User Journeys	System Ecosystems	Content / Programme Audits MVP v MLP* Service Blueprint	Paper prototyping Clickable prototype initial dev	Clickable prototypes Preparing tests	Testing prototypes Feedback capture & Analysis	Testing prototypes Feedback capture & Analysis	Prioritization Further dev based on testing	Concept presentations Playback Report with insights and areas for development

*Minimum Lovable Product

Weekly overview

PREPARE	RESEARCH				DESIGN					WRAP-UP	
	DISCOVER		EXPLORE		DEVELOP			DELIVER			
Week Z 01 - 05 Feb	Week 0 08-12 Feb	Week 1 15-19 Feb	Week 2 22-26 Feb	Week 3 01-05 Mar	Week 4 08-12 Mar	Week 5 15-19 Mar	Week 6 22-26 Mar	Week 7 29-02 Apr	Week 8 06 - 09 Apr	Week 9 12-16 Apr	Week 10 19-23 Apr
Catalyst welcome event Team meeting Admin	1:1 meetings Project initiation	Kick-off workshop Audience analysis	Architecture Of Participation User Journeys	System Ecosystems	Content / Programme Audits MVP v MLP* Service Blueprint	Paper prototyping Clickable prototype initial dev	Clickable prototypes Preparing tests	Testing prototypes Feedback capture & Analysis	Testing prototypes Feedback capture & Analysis Prioritization	User stories Further dev based on testing	Concept presentations Playback Report with insights and areas for development

*Minimum Lovable Product

Weekly overview

PREPARE	RESEARCH				DELIVER				WRAP-UP		
	DISCOVER		EXPLORE		DEVELOP		DELIVER				
Week Z 01 - 05 Feb	Week 0 08-12 Feb	Week 1 15-19 Feb	Week 2 22-26 Feb	Week 3 01-05 Mar	Week 4 08-12 Mar	Week 5 15-19 Mar	Week 6 22-26 Mar	Week 7 29-02 Apr	Week 8 06 - 09 Apr	Week 9 12-16 Apr	Week 10 19-23 Apr
Catalyst welcome event Team meeting Admin	1:1 meetings Project initiation	Kick-off workshop Audience analysis	Architecture Of Participation User Journeys	System Ecosystem s	Content / Programme Audits MVP v MLP* Service Blueprint	Paper prototyping Clickable prototype initial dev	Clickable prototypes Preparing tests	Testing prototypes Feedback capture & Analysis	User stories Prioritization	Concept presentati ons	Playback Reports

*Minimum Lovable Product

Weekly overview

PREPARE	RESEARCH				DELIVER				WRAP-UP		
	DISCOVER		EXPLORE		DEVELOP		DELIVER				
Week Z 01 - 05 Feb	Week 0 08-12 Feb	Week 1 15-19 Feb	Week 2 22-26 Feb	Week 3 01-05 Mar	Week 4 08-12 Mar	Week 5 15-19 Mar	Week 6 22-26 Mar	Week 7 29-02 Apr	Week 8 06 - 09 Apr	Week 9 12-16 Apr	Week 10 19-23 Apr
Catalyst welcome event Team meeting Admin	1:1 meetings Project initiation	Kick-off workshop Audience analysis	Architecture Of Participation User Journeys	System Ecosystem s Service Blueprint	Content / Programme Audits MVP v MLP*	Paper prototyping Clickable prototype initial dev	Clickable prototypes Preparing tests	Testing prototypes Feedback capture & Analysis	User stories Prioritization	Concept presentati ons	Playback Reports

*Minimum Lovable Product

Weekly overview

PREPARE	RESEARCH				DESIGN				DELIVER		WRAP-UP
	DISCOVER	EXPLORE	DEFINE	DEVELOP	CONCEPT	PROTOTYPE	TEST	IMPLEMENT			
Week Z 01 - 05 Feb	Week 0 08-12 Feb	Week 1 15-19 Feb	Week 2 22-26 Feb	Week 3 01-05 Mar	Week 4 08-12 Mar	Week 5 15-19 Mar	Week 6 22-26 Mar	Week 7 29-02 Apr	Week 8 06 - 09 Apr	Week 9 12-16 Apr	Week 10 19-23 Apr
Catalyst welcome event Team meeting Admin	1:1 meetings Project initiation	Kick-off workshop Audience analysis	Architecture Of Participation User Journeys	Content / Programme Audits MVP v MLP*	System Ecosystems Service Blueprint	Paper prototyping Clickable prototype initial dev	Clickable prototypes Preparing tests	Testing prototypes Feedback capture & Analysis	User stories Prioritization	Concept presentations	Playback Reports

*Minimum Lovable Product

Weekly overview

PREPARE	RESEARCH				DESIGN				WRAP-UP	
	DISCOVER		DEFINE		DEVELOP		DELIVER			
Week 0 01 - 05 Feb	Week 1 08-12 Feb	Week 2 15-19 Feb	Week 3 22-26 Feb	Week 4 05 Mar	Week 5 12-16 Mar	Week 6 15-19 Mar	Week 7 29-01 Apr	Week 8 06-09 Apr	Week 9 12-16 Apr	Week 10 19-23 Apr
Catalyst welcome event	Project initiation	Project workshop	Jobsys	Content Audits	Defining MLP*	Testing of prototypes	Analysis of feedback	Clickable prototypes	Further dev based on testing	Concept presentations
Team meeting	1:1 meetings with charities	Discovery review	Architecture Of Participation	System Ecosystem	Service Blueprint	Feedback capture	Iteration workshop	User stories	Prioritization	Report with insights and areas for development
Admin (contracts, etc.)		Audience analysis			Paper prototyping		Clickable prototype initial dev			

*Minimum Lovable Product
